



## The Kenilworth Beach Improvement Project Weekly Construction Progress Update – 9/19/2025

### 1. Work Completed this Week

- Mobilization of Bulley & Andrews site Superintendent
- Perimeter fence was installed around the site
- Beach matting was laid down to allow for trucks and machinery to access the site more easily.
- Disconnection of electrical and plumbing services to make the site safe for demolition.

### 2. Work Planned for Next Week

- Site Demolition to begin on Monday September 22<sup>nd</sup>

### 3. Coordination & Issues

- Safety: No incidents, no injuries
- Delays: No delays
- Inspections/Permits: No inspections performed this week.

### 4. Photos & Visuals - (attached)



**Description**

Project Sign on perimeter fencing

**Taken Date**

09/16/2025 at 11:53 am

**Uploaded By**

Shamus McLaughlin

**Description**



**Description**


Additional view of perimeter fence on Kenilworth Avenue

**Taken Date**

09/17/2025 at 11:46 am

**Uploaded By**

Shamus McLauhlin

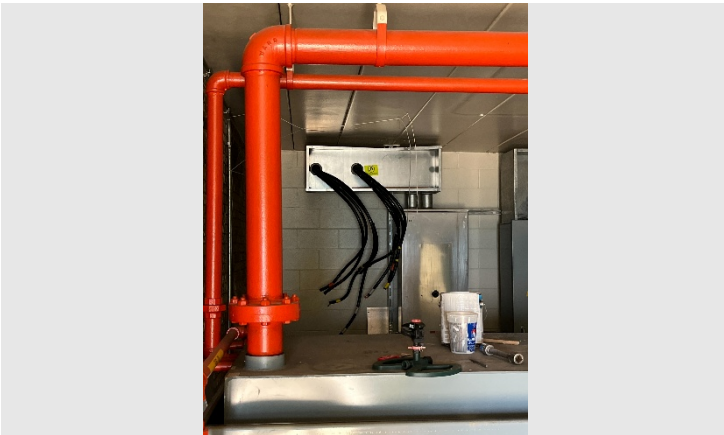

**Description**


Electrical disconnects in the generator room.

**Taken Date**

09/18/2025 at 10:31 am

**Uploaded By**

Shamus McLaughlin

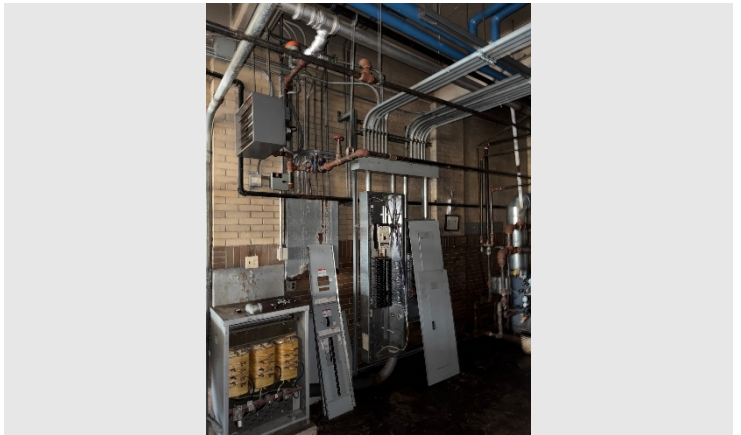

**Description**


Disconnection of main electrical panels inside the water treatment plant.

**Taken Date**

09/17/2025 at 09:23 am

**Uploaded By**

Patrick Jones

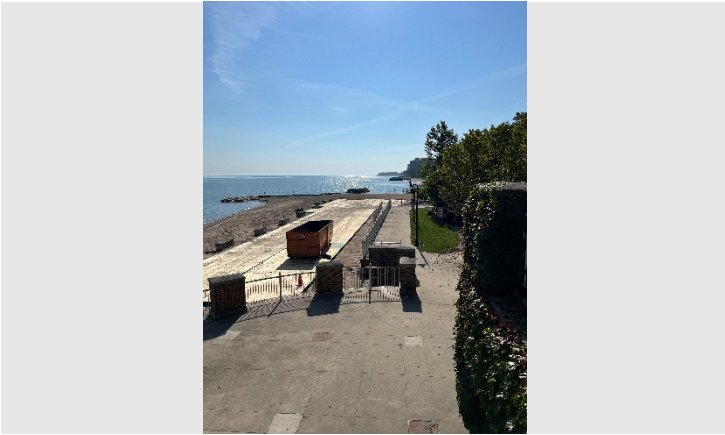

**Description**


Picture looking at mats laid to protect the beach and allow access to the site for machinery.

**Taken Date**

09/18/2025 at 08:23 am

**Uploaded By**

Patrick Jones

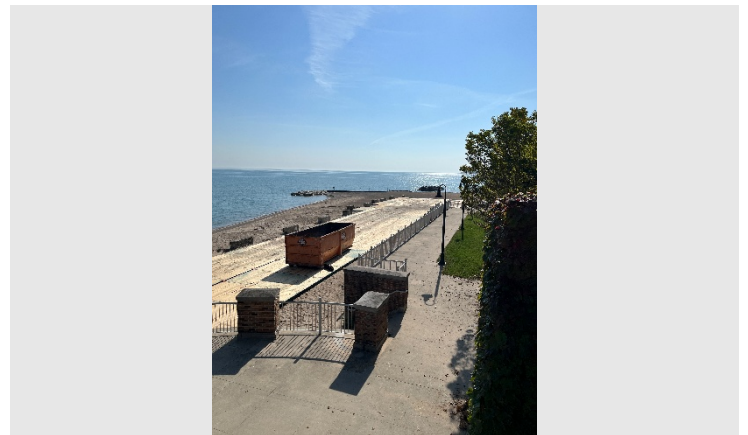

**Description**

Picture of a dumpster placed on the mats for site debris.

**Taken Date**

09/18/2025 at 07:55 am

**Uploaded By**

Sjhamus McLaughlin
