

# **BULLEY & ANDREWS**

## **The Kenilworth Beach Improvement Project Weekly Construction Progress Update – 4/03/2026**

### **1. Work Completed this Week.**

- Bathroom building roof deck work continued this week.
- Electric work continued this week.
- Plumbing continued this week.
- Coordination among trades continues, including concrete, steel, plumber, and electricians.

### **2. Work Planned for Next Week**

- Additional concrete framing and pouring for stairs and slab on grade concrete.
- Electrical and plumbing will continue.
- Waterproofing seal and back fill backfill upper retaining walls.

### **3. Coordination & Issues**

- Safety: No incidents or injuries reported
- Delays: One weather day occurred this week because of rain

### **4. Photos**

- Attached for reference



Figure 1: Curb installed on roof top deck.




Figure 2: Additional view of the roof top and new windows installed.



**Figure 3: the roof deck of the bathroom building looking east.**



**Figure 4: Back fill for the concrete ramp.**

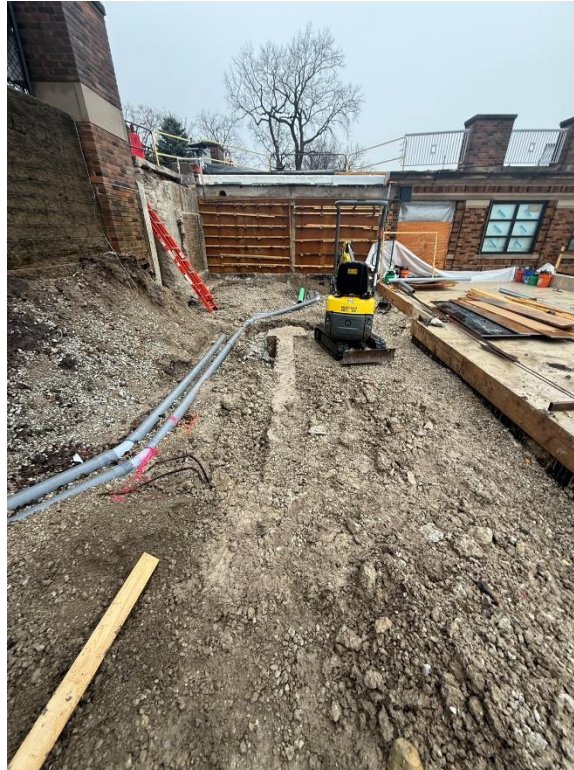

**Figure 5: Preparing upper level for ramp steel.**



**Figure 6: Preparing the ramp for concrete walkway.**



**Figure 7: View of the bottom of the ramp facing south.**
