



## The Kenilworth Beach Improvement Project Weekly Construction Progress Update – 10/03/2025

### 1. Work Completed this Week

- Demolition of interior electrical equipment continued this week.
- Masonry demolition to accommodate the salvage and reuse of building brick.
- Coordination of Lake Michigan and tree protection to be in place the week of 10/06/2025 before heavy demolition begins.
- Control points for the excavator, helical piers, and concrete footings established to allow for excavation to begin.

### 2. Work Planned for Next Week

- MWRD protections to be installed (tree and water protection).
- MWRD to inspect and approve protections.
- Excavation to begin.
- Heavy demolition to begin.


### 3. Coordination & Issues

- Safety: No incidents, no injuries
- Delays: No delays to report
- Inspections/Permits: No inspections performed this week

### 4. Photos & Visuals - (attached)



**Figure 1: Removal of electrical equipment within main building.**

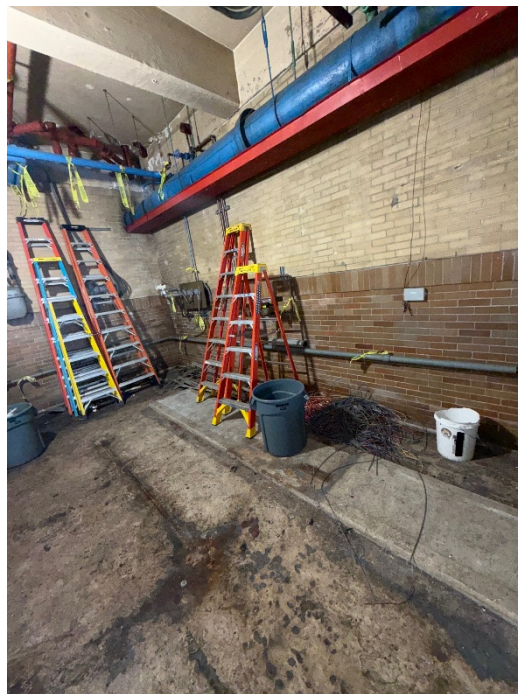

**Figure 2: Additional view of removed electrical equipment inside new mechanical space.**



**Figure 3: View of mechanical room facing west.**



**Figure 4: Photo of Masonry demolition being done to salvage brick to be reused on site.**



**Figure 5: View of masonry removed to allow the removal of the existing lift.**



**Figure 6: View of material put over stone to accommodate heavier machinery accessing the ramp area on the beach.**



Figure 7: Removal of racks to allow demolition to occur.



Figure 8: View of area with racks removed.



**Figure 9: New temporary ramp for heavy machinery.**



**Figure 10: Placement of mats to keep ramp stone in place.**
