



The Kenilworth Beach Improvement Project Weekly Construction Progress Update – 10/10/2025

1. Work Completed this Week.

- MWRD granted approval to proceed with continued demolition and excavation activities under the existing site control measures.
- Completed demolition and removal of the wooden structure located on the north side of the site.
- Initiated and advanced demolition of the brick structure situated east of the main building, with significant progress made this week.
- Additional excavation equipment was mobilized and staged on-site to support ongoing earthwork operations.

2. Work Planned for Next Week

- Excavation to continue.
- Heavy demolition continues.

3. Coordination & Issues

- Safety: No incidents, no injuries
- Delays: No delays to report
- Inspections: Conducted inspection of erosion control measures; work was reviewed and approved to proceed.

4. Photos & Visuals - (attached)



Figure 1: Protective plates placed to protect concrete that will remain.

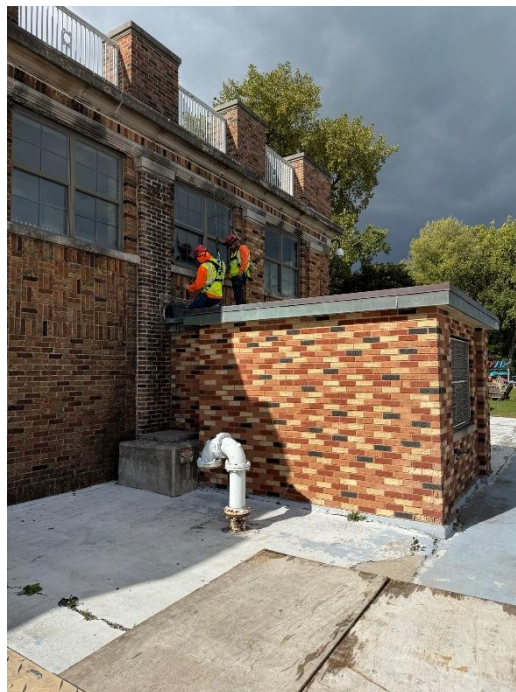


Figure 2: Disconnecting roofing material from main building.



Figure 3: Removing roofing from connected wood structure.



Figure 4: Wood structure being removed on north side of the building.

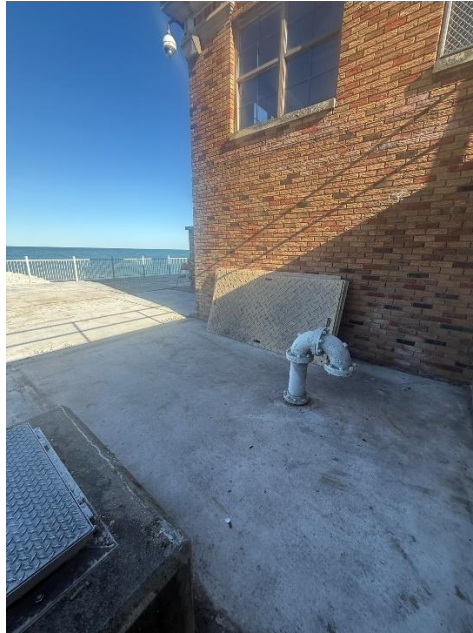


Figure 5: Wood structure completely removed.

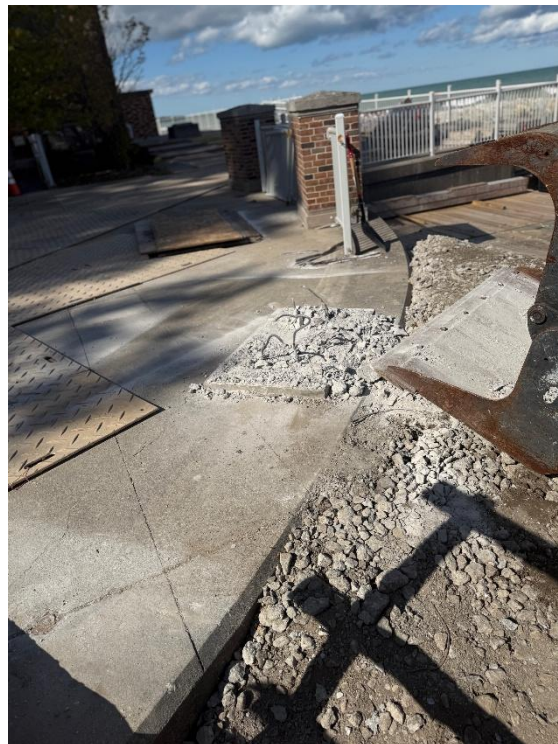


Figure 6: Demolition conducted to allow access for larger machinery needed for excavation.



Figure 7: Brick removed from east side structure.



Figure 8: Additional view of east side structure.
