



## The Kenilworth Beach Improvement Project Weekly Construction Progress Update – 11/07/2025

### 1. Work Completed this Week.

- Demolition of south side structures and concrete steps has been completed.
- Vegetation removal along the bluff has been completed.
- Excavation and concrete removal on the south end of the site have been performed.
- Coordination among trades continues, including excavation, concrete, and helical pier installation activities.

### 2. Work Planned for Next Week

- Excavation to continue,
- Preparing the area for helical piers to support the new ramp.

### 3. Coordination & Issues

- Safety: No incidents, no injuries
- Delays: No delays to report


### 4. Photos & Visuals - (attached)



**Figure 1: Demolition continues.**



**Figure 2: Concrete deck removed by the demolition contractor.**

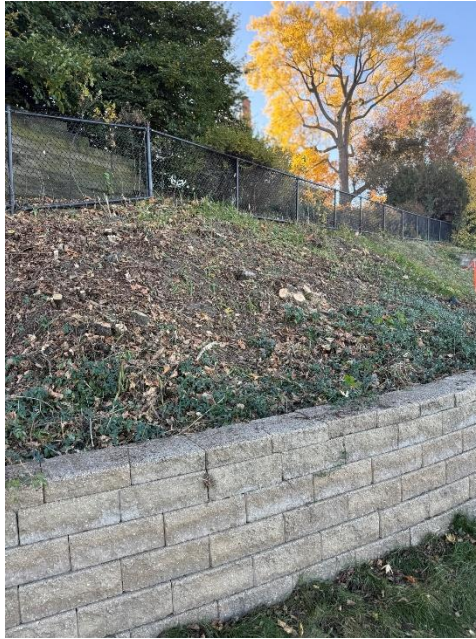

**Figure 3: View of vegetation on the bluff removed to allow excavation to continue.**



**Figure 4: Excavation of the southern area in front of the bluff.**




**Figure 5: Area being prepared for helical piers to be installed the week of 11/10.**



**Figure 6: Demolition of southern area to make way for new ramp.**



**Figure 7: Demolition of area south of building for new foundation of bathroom building.**

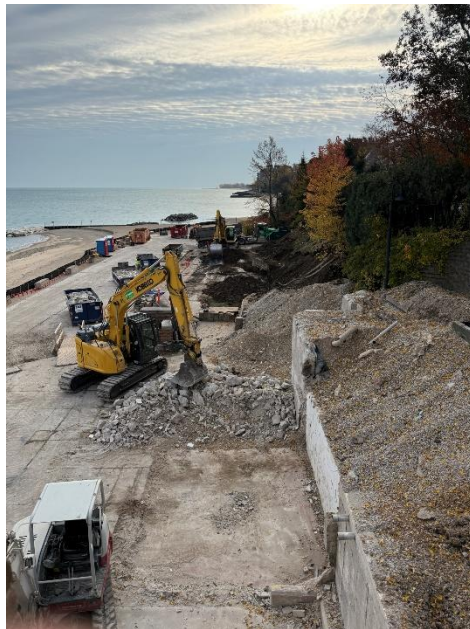

**Figure 8: Demolition and excavation on southern portion of the site.**



**Figure 9: Demolition of area on the south portion of the site facing north.**
