

BULLEY & ANDREWS

The Kenilworth Beach Improvement Project Weekly Construction Progress Update – 1/16/2026

1. Work Completed this Week.

- Additional foundations forms set for concrete pour
- Rebar installed in forms
- Coordination among trades continues, including concrete work and steel preparation

2. Work Planned for Next Week

- Pour concrete foundation walls
- Plumber to begin doing underground piping
- Electricians will continue to run wiring for new lighting and outlets

3. Coordination & Issues

- Safety: No incidents or injuries reported
- Delays: Two lost weather delays occurred week of 1/12

4. Coordination & Issues

- Attached for reference



Figure 1: Aerial view of the site facing north.



Figure 2: Aerial view of the site facing west.



Figure 3: Framing for the foundation walls on the south end of the site.



Figure 4: Framing and foundations being prepared for concrete pour.



Figure 5: Foundation wall framing being installed.

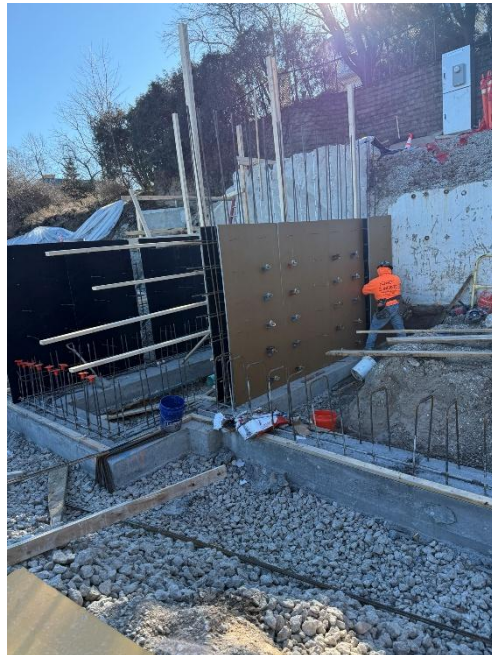


Figure 6: Framing and rebar being installed for new stairs.



Figure 7: Additional view of rebar in concrete forms.



Figure 8: Addition view of forms for new stairs being installed.
