



## The Kenilworth Beach Improvement Project Weekly Construction Progress Update – 2/13/2026

### 1. Work Completed this Week.

- Concrete was poured by the subcontractor this week.
- Heating the subcontractor deployed units to assist with ground thaw to accommodate additional concrete pours.
- Forms will be removed to allow for water proofing.
- Coordination among trades continues, including concrete, steel, and carpenter.

### 2. Work Planned for Next Week

- Backfill the areas around the concrete pours.
- Waterproofing of poured concrete.
- Plumber will continue installing under slab plumbing for new bath house.

### 3. Coordination & Issues


- Safety: No incidents or injuries reported
- Delays: No additional delays in the week of 2/09/26.

### 4. Photos

- Attached for reference



**Figure 1: Pumping the concrete into the concrete forms.**

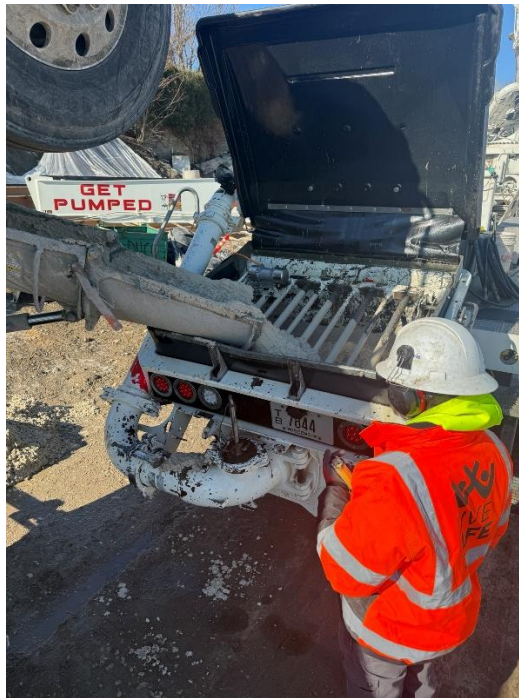

**Figure 2: Loading pump truck with concrete.**



**Figure 3: Concrete pump truck delivering concrete to the new stair well.**



**Figure 4: View of concrete forms blanketed to protect form the wind and the cold.**



**Figure 5: Blanketed concrete forms on the south end of the site.**



**Figure 6: View of stairway walls poured and blanketed.**



**Figure 7: Poured and blanketed concrete foundation on the south side of the site building.**



**Figure 8: Addition view of blanketed concrete forms.**
