



## The Kenilworth Beach Improvement Project Weekly Construction Progress Update – 3/06/2026

### 1. Work Completed this Week.

- Continuing with backfilling of earth was done this week behind concrete pours from last week.
- Waterproofing of concrete was performed on concrete poured last week.
- Concrete framing was installed for next week's pour.
- Steel for the bathroom building was delivered and installed.
- Coordination among trades continues, including concrete, steel, and plumber.

### 2. Work Planned for Next Week

- Additional concrete framing.
- Concrete pours will continue next week.
- Plumber will continue installing under slab plumbing for new bath house.

### 3. Coordination & Issues

- Safety: No incidents or injuries reported
- Delays: No additional delays in the week of 3/02/26.

### 4. Photos

- Attached for reference



**Figure 1: Building area being prepared for installation of steel beams.**



**Figure 2: Steel framing installed in the new Bathroom building.**




**Figure 3: Additional picture of steel installed for the bathroom building.**



**Figure 4: View of concrete ramp walls.**



**Figure 5: New ramp and backfilling activities.**

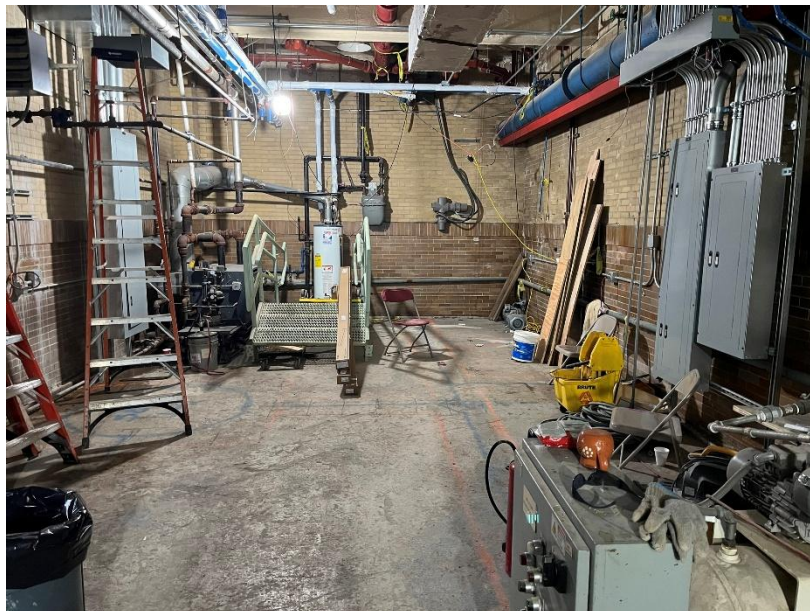

**Figure 6: Mechanical space floor spray painted in preparation for saw cutting to begin next week.**
