

# **BULLEY & ANDREWS**

## **The Kenilworth Beach Improvement Project Weekly Construction Progress Update – 3/13/2026**

### **1. Work Completed this Week.**

- Concrete framing was installed for next week's concrete pour.
- Plumbers installed underground piping for the new Bathhouse and inside the new mechanical space.
- Areas for new concrete pads were prepared this week.
- Coordination among trades continues, including concrete, steel, and plumber.

### **2. Work Planned for Next Week**


- Additional concrete framing.
- Concrete pours will continue next week.
- Plumbers will continue installing plumbing for new bath house.

### **3. Coordination & Issues**

- Safety: No incidents or injuries reported
- Delays: No additional delays in the week of 3/09/26.

### **4. Photos**

- Attached for reference

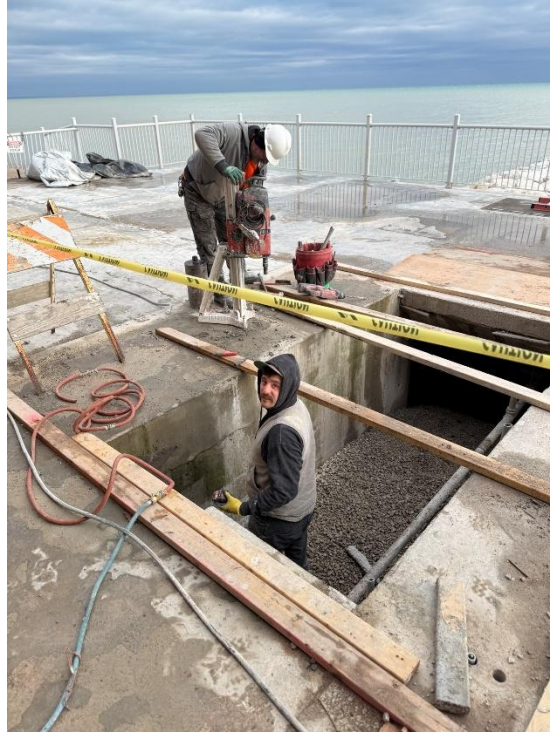

**Figure 1: Building area on the east side is being prepared to receive new concrete.**



**Figure 2: Area on the north side of the building that will have new concrete.**

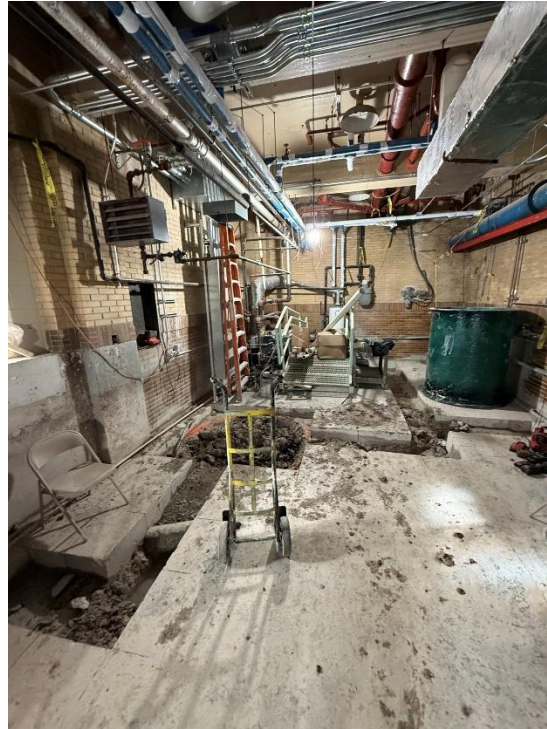


Figure 3: Photo of saw cut concrete floor to accommodate new plumbing rough in.



Figure 4: Install underground plumbing in the new Bathhouse.



**Figure 5: Framing for more concrete that will be poured.**



**Figure 6: Preparing the roof of the Bathhouse.**



Figure 7: Overhead site photos.

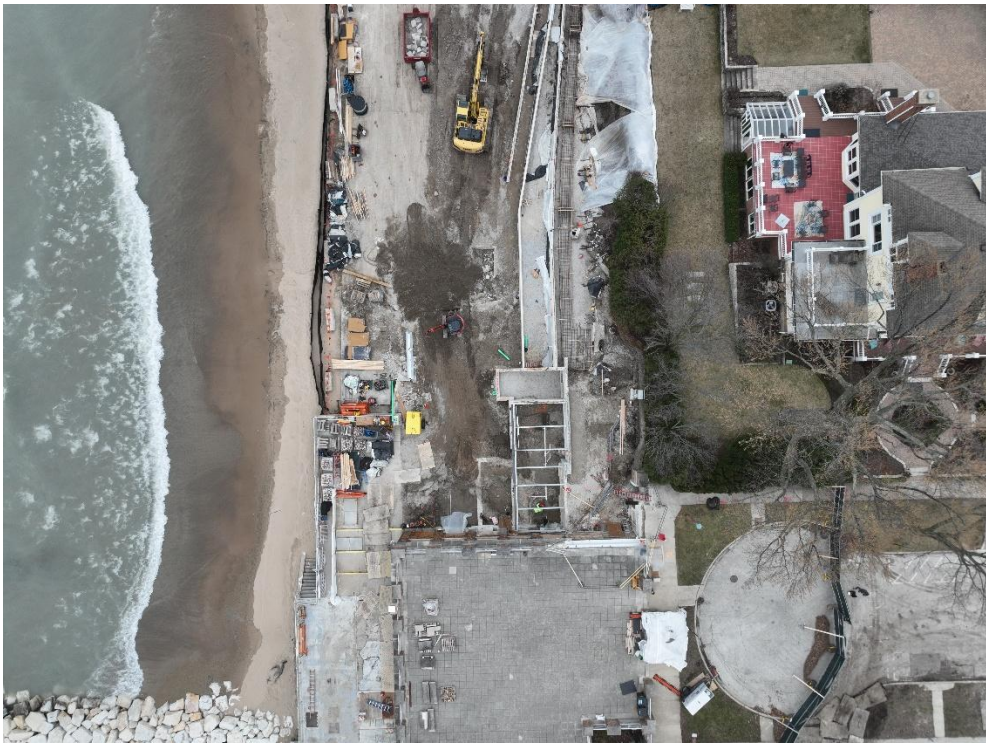


Figure 8: Overhead site photos.
