

# **BULLEY & ANDREWS**

## **The Kenilworth Beach Improvement Project Weekly Construction Progress Update – 3/20/2026**

### **1. Work Completed this Week.**

- Site restoration work.
- Concrete framing was installed for next week's concrete pour at south end of retaining walls.
- Plumbers installed underground piping for the new bathroom building and inside the new mechanical space including new concrete pad and housing for sewage ejector pit installation.
- Rooftop of bathroom building framed for concrete pour.
- Coordination among trades continues, including concrete, steel, plumber and electricians.

### **2. Work Planned for Next Week**


- Additional concrete framing and pouring.
- Anchor bolt survey
- Window installation
- Seal and backfill upper retaining walls

### **3. Coordination & Issues**

- Safety: No incidents or injuries reported
- Delays: Severe windstorm over the weekend caused significant damage to the jobsite. Site grading and leveling was performed, replacement of multiple sections of crane matting was completed, and wave dissipating concrete blocks were leveled and adjusted. The site was restored to working order by end of day Wednesday 3/18/26.

### **4. Photos**

- Attached for reference

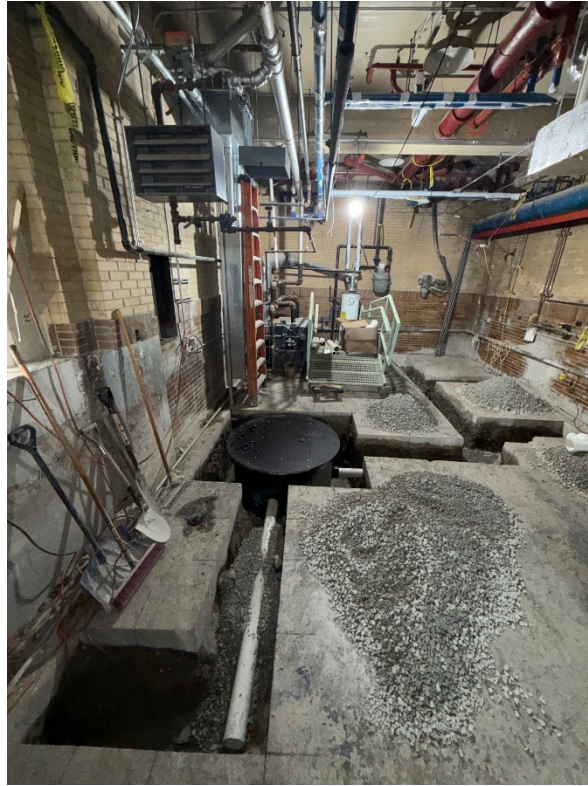

**Figure 1: Sewage Ejector Pit Install.**



**Figure 2: Sewage Ejector Pit and Saw cutting.**



**Figure 3: Roof Framing of Bathroom Building.**



**Figure 4: Roof Framing of Bathroom Building.**



**Figure 5: Damaged Site Matting.**



**Figure 6: Repaired Site Matting.**



Figure 7: Overhead site photos.



Figure 8: Overhead site photos.
