

BULLEY & ANDREWS

The Kenilworth Beach Improvement Project Weekly Construction Progress Update – 3/27/2026

1. Work Completed this Week.

- Bathroom Building roof concrete was poured this week.
- Windows were installed this week.
- Injector pit in the maintenance room was installed and backfilled this week.
- Coordination among trades continues, including concrete, steel, plumber and electricians.

2. Work Planned for Next Week

- Additional concrete framing and pouring.
- Anchor bolt survey.
- Waterproofing seal and back fill backfill upper retaining walls.

3. Coordination & Issues

- Safety: No incidents or injuries reported
- Delays: No delays on account of weather this week

4. Photos

- Attached for reference



Figure 1: Inside the new bathroom building.



Figure 2: Inside the new bathroom building from another view.

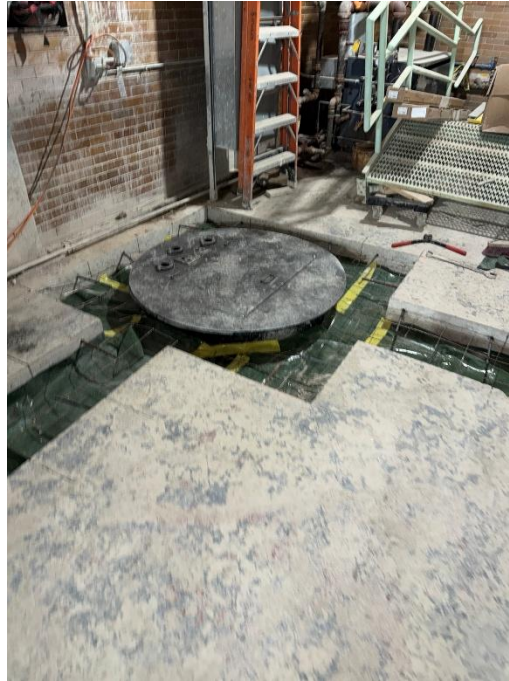


Figure 3: Injector pit backfilled and ready for concrete.

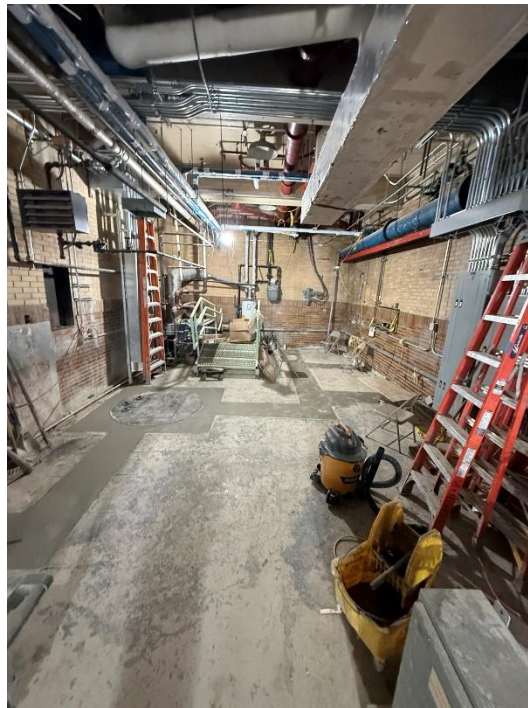


Figure 4: Concrete poured in maintenance room.



Figure 5: Additional framing for concrete.



Figure 6: Ramp wall and foundations.



Figure 7: Roof above bathroom building.



Figure 8: Concrete roof above bathroom building.



Figure 5: Additional framing for concrete.



Figure 6: Ramp wall and foundations.



Figure 9: Windows being installed.



Figure 10: New windows installed.
